

📅 WEDNESDAY, MAY 14, 2025

Test - Complete Dye Test

Performed a complete dye test.




Test - Pressure Test - Leak Detection

All lines are holding solidAdditional Notes: Alternative testing on all returns Passed



Deck/Surface/Equipment

Deck:Pavers Surface:Pebble tec

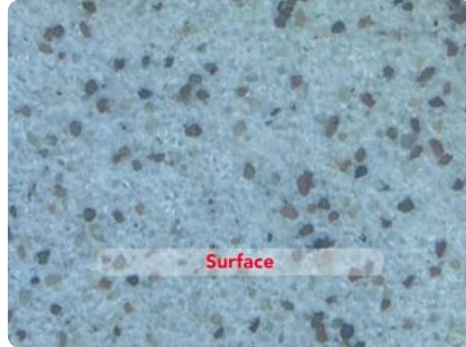

Leak Status - Equipment Leak

The equipment will leak, as identified in the findings, until it is fixed by a pool service professional.



Epoxy - Item Previously Epoxied

Found existing epoxy patch: In and around the light Around the return In the tile In and around the vac line Epoxy patches can be an indication of previous leaks that could open up in the future, initiating further water loss. Epoxy patches are an indication of previous leaks that could open up in the future as the patch wears away, initiating further water loss. Recommend proper repair. Additional Notes: Wall port closed with Epoxy




Miscellaneous




Test - Water Loss - Set Up

Water level marked in: Zero Results will be confirmed by: Phone call
Date of confirmation: 2025-05-15
Additional Notes: Pump off

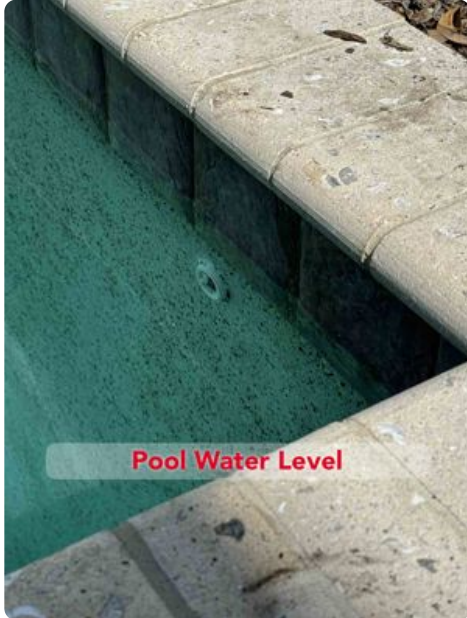

Pool Water Level

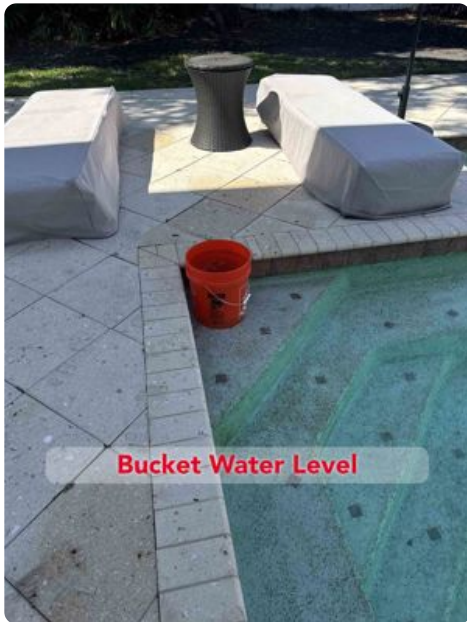

Bucket Water Level



📅 THURSDAY, MAY 15, 2025

Test - Water Loss - Results - Not Leaking

Confirmed water level is holding solid. The pool is not leaking. Evaporation and equipment leak.

